





Education is the Key to Success our schools. Our community. Our future.

## 



#### SCHEDULING KEY FACTORS





- » Understand the lead times of all products (having all materials ready make the projects move smoothly)
- » Arrange projects based on Subcontractor types (so that there is an efficiency in costs and 'man'power)
- » Understand the needs / wants of the Community (Fields and Grade Re-alignment)
- » Timing The later the Bid the higher the price (moreso for time restricted work)
- » SA last recommended bid release date = January 15th (for summer work)





### POST-REFERENDUM SCHEDULE



<b>BOGOTA</b>	REFERENDUM	SCHEDULE
---------------	------------	----------

	DESIGN START	CONSTRUCTION	CONSTRUCTION END	NOTES
PROJECT #1				
FIELDS				
Redesign and provide field upgrades to the High School Stadium Field inclusive of new lighting and bleachers	4/1/2023-12/1/2023	3/2024	9/2024	
Redesign and provide field upgrades to the Baseball Field / Softball Field	4/1/2023-12/1/2023	6/2024	9/2024	Baseball season ends in june, may need to cut the season short
PROJECT #2				
Lodge Renovations - 5 Vocational Classrooms				
5 Vocational Classroom Renovations	5/1/2023 - 12/2023	1/2024	1/2025	May not open until Sept 2025; Schedule may adjust based on design details
PROJECT #3				
Classroom Renovations (to convert to age appropriate)				
Art Room Renovation - Room 127 - (Minor modifications and new furniture; UVs and existing ceiling, flooring and lights to remain)	5/1/2023 - 10/2023	6/2024	9/2024	Possible to redistrict by 9/24 without Gym Renovations
Music Room Renovation - Room 211 - (Minor modifications and new furniture; UVs and existing ceiling, flooring and lights to remain)				
Pre-k and Kindergarten Classroom Toilet Renovations - Rms 118, 105, 106, B22, B23 (Minor modifications and new toilet room; UVs and existing ceiling, flooring and lights to remain)				



## POST-REFERENDUM SCHEDULE



PROJECT #4				
Gymnasium Renovation - (Enlarge space by moving stage into Music Room Addition)	10/1/2023 - 2/2024	5/2025	9/2025	May need to close the GYM for May/June
PROJECT #5				
BIXBY Upgrade Electrical				
Replace antiquated panelboards BIXBY	40/4/2022 2/2024	6/2025	9/2025	This will likely be tied in with the Gym Renovations; Long lead for panels
Electrical Service Upgrade BIXBY	10/1/2023 - 2/2024			
STEEN Upgrade Electrical				
Replace antiquated panelboards STEEN	10/1/2023 - 2/2024		0/2025	Steen / HS work together; Long lead for panels
Electrical Service Upgrade STEEN		6/2025	9/2025	
JR. SR. HS Upgrade Electrical	<u> </u>			
Electrical Service Upgrade JR. SR. HS	10/1/2023 - 2/2024		9/2025	Steen / HS work together; Long lead for panels
Replace antiquated panelboards JR. SR. HS		6/2025		
PROJECT #6	1			
Toilet Room Renovations				
Renovate the two Lower Level Faculty Toilet Rooms in order to provide the proper toilet room fixture count for the building (2 gang toilets for 500 sf)	7/1/2023 - 11/2023	6/2024	9/2024	
Renovate Level One Girl's Toilet to provide new finishes and ADA accessibility (1 small gang toilet for 100 sf total)				
Renovate the Boy's and Girl's Cafeteria Toilets to provide new finishes and ADA accessibility (2 small gang toilets for 150 sf)				
Renovate Level Two Girl's Toilet to provide new finishes and ADA accessibility (1 gang toilet for 250 sf)				



## POST-REFERENDUM SCHEDULE



PROJECT #7						
Renovate Auditorium						
Renovate the Auditorium & Balcony to allow for the additional Staff and Student demands of the school	6/1/2024 - 11/2024	6/2025	9/2025			
PROJECT #8						
Renovate Media Center						
Renovate the Media Center to better suite the needs of the current curriculum - flooring, lighting, casework, furniture	4/1/2025 - 10/2025	6/2026	9/2026			
PROJECT #9						
Classroom Renovations STEEN						
Art Room Renovation	4/1/2025 - 10/2025	6/2026	9/2026			

## 



#### WORK COMPLETED TO DATE





- » Complete Topographic Survey of the property
- » Geotechnical testing of the soil
- » Layout of the proposed design on the updated accurate survey
- » Meetings with Administration to determine suggested design



#### FIELDS - NEXT STEPS / TIMELINE



#### June/July

- » Locate deeds related to town property line to confirm parking will remain outside of the project
- » Meet with Town administration to present design and solicit input
- » Determine the best solution for Storage on the property

#### August

- » Complete Design and create updated design renderings
- » Complete Stormwater Design and submit to Planning Board for courtesy review

#### September

- » Submit to DEP Dept of Environmental Protection
- » Complete remaining Construction Documents
- » WAIT 90 days minimum

#### December '23 /January '24

» Public Bidding Process

#### March – September '24

» Construction of High School Stadium Field inclusive of new lighting and bleachers

#### June – September '24

» Construction of Baseball and Softball Fields



## CTEBUILDING





#### CTE PROGRAMS - COMMUNITY SURVEY

Now that the Referendum has passed, the District is looking for the community's help with coming up with the most desirable programs for the Career Technical building. The district has identified several CTE categories that hold great potential for our students' success as well as the for the community. In order to prioritize and determine the most relevant and impactful options, we would like the community's input.

Your participation in evaluating these categories is crucial. By sharing your perspectives and insights, you will help shape the future of the CTE School. We want to ensure that the selected categories align with the needs and aspirations of our students, preparing them for thriving careers.


Together, we will choose the top five CTE categories that will be developed in the upcoming school. Your ratings will provide valuable input that drives our decision-making process and paves the way for a transformative educational experience.



#### POTENTIAL PROGRAMS



- » Automotive Technology
- » Cosmetology
- » Culinary Arts
- » Education and Human Services & Child Development
- » Engineering / Architecture
- » Finance
- » Health and Medical Sciences
- » Information Technology
- » Mechanical, Electrical, Plumbing (MEP)
- » Performing Arts

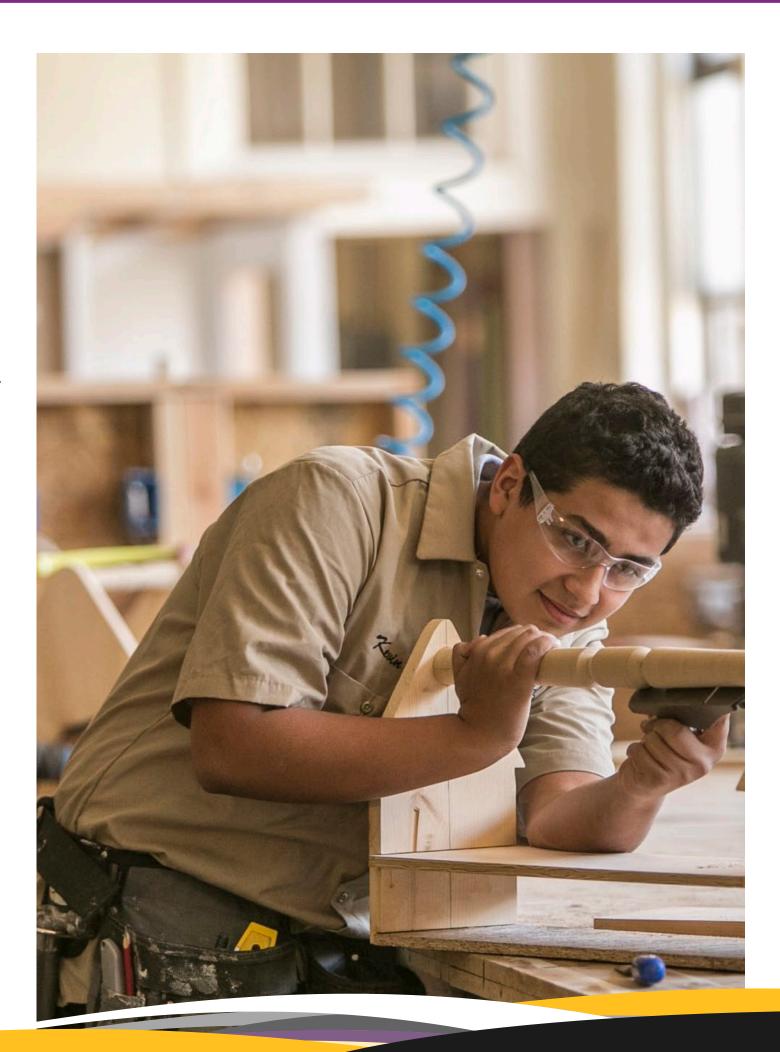



#### CTE BUILDING TIMELINE



#### June/July

Send out Community Survey and collect and sort the data

#### **August**

- » Finalize Schematic Design and layouts based on selected programs
- » Determine the basis of design for MEP Systems

#### September/ October

- » Complete Design and create updated design renderings
- » Complete remaining Construction Documents

#### November / December

» Public Bidding Process

#### January '24 - December '24

» Gut renovation of building and construction of 5 CTE classrooms



# GRADE ALIGNMENT BIXBY SCHOOL

PROPOSED GRADE RE-ALIGNMENT

E ROY BIXBY SCHOOL PK-2

LILLIAN M STEEN SCHOOL 3-6

BOGOTA MIDDLE SCHOOL 7-8 BOGOTA HIGH SCHOOL 9-12







#### BIXBY SCHOOL TIMELINE



#### June/July

- » Layout basic design concepts
- » Review with School Administration
- » Determine the basis of design for MEP Systems

#### **August**

» Complete Design and create updated design renderings

#### September

» Complete remaining Construction Documents

#### October

» Public Bidding Process


#### June'24 - September '24

» Complete renovation of 7 classrooms to allow for re-alignment





## HIGH SCHOOL TOILETS



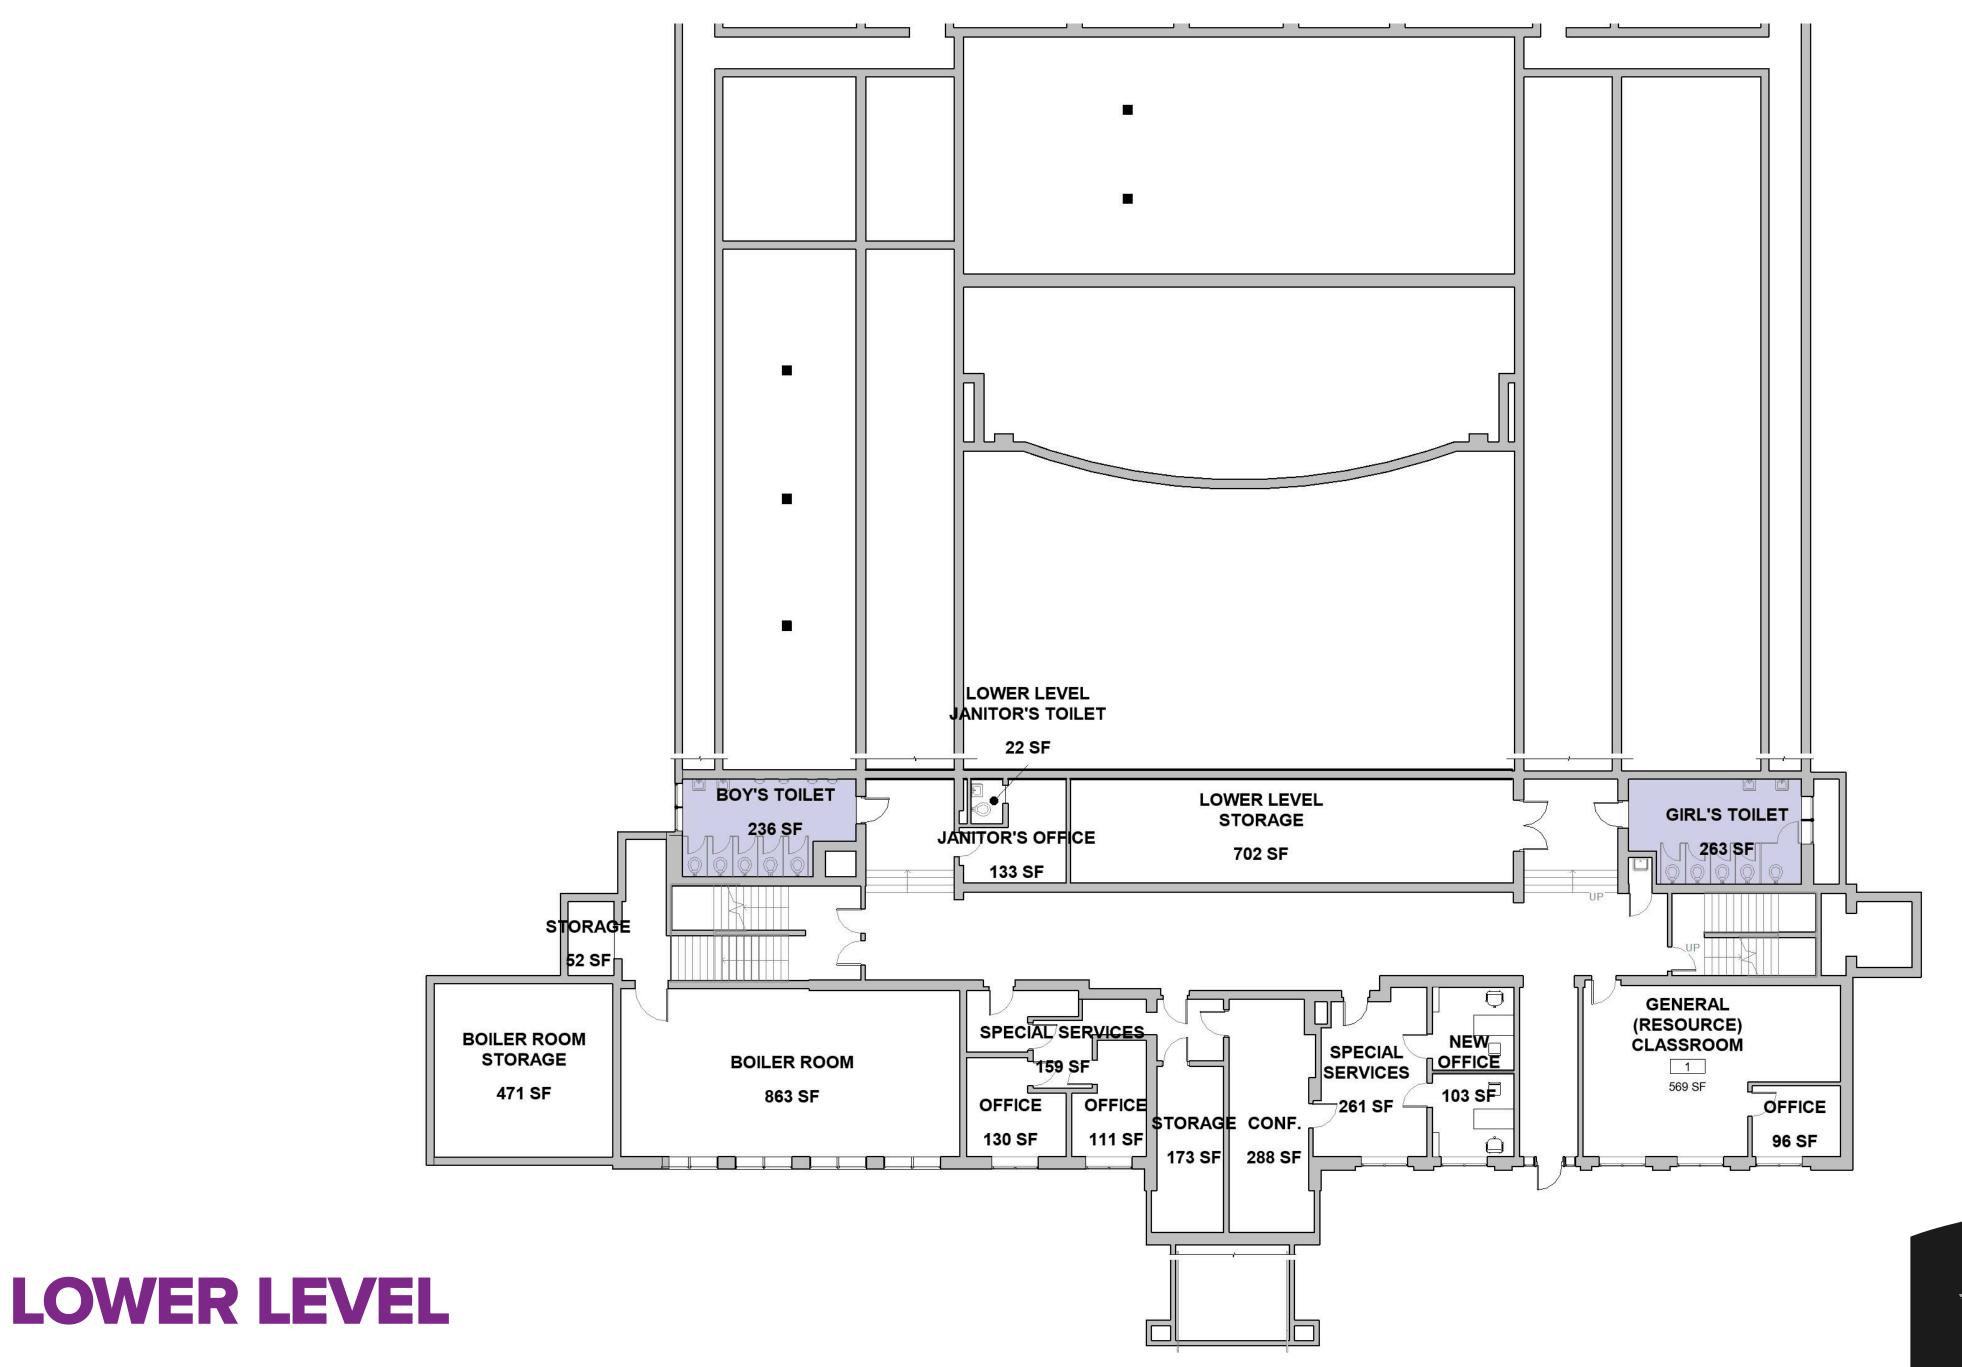



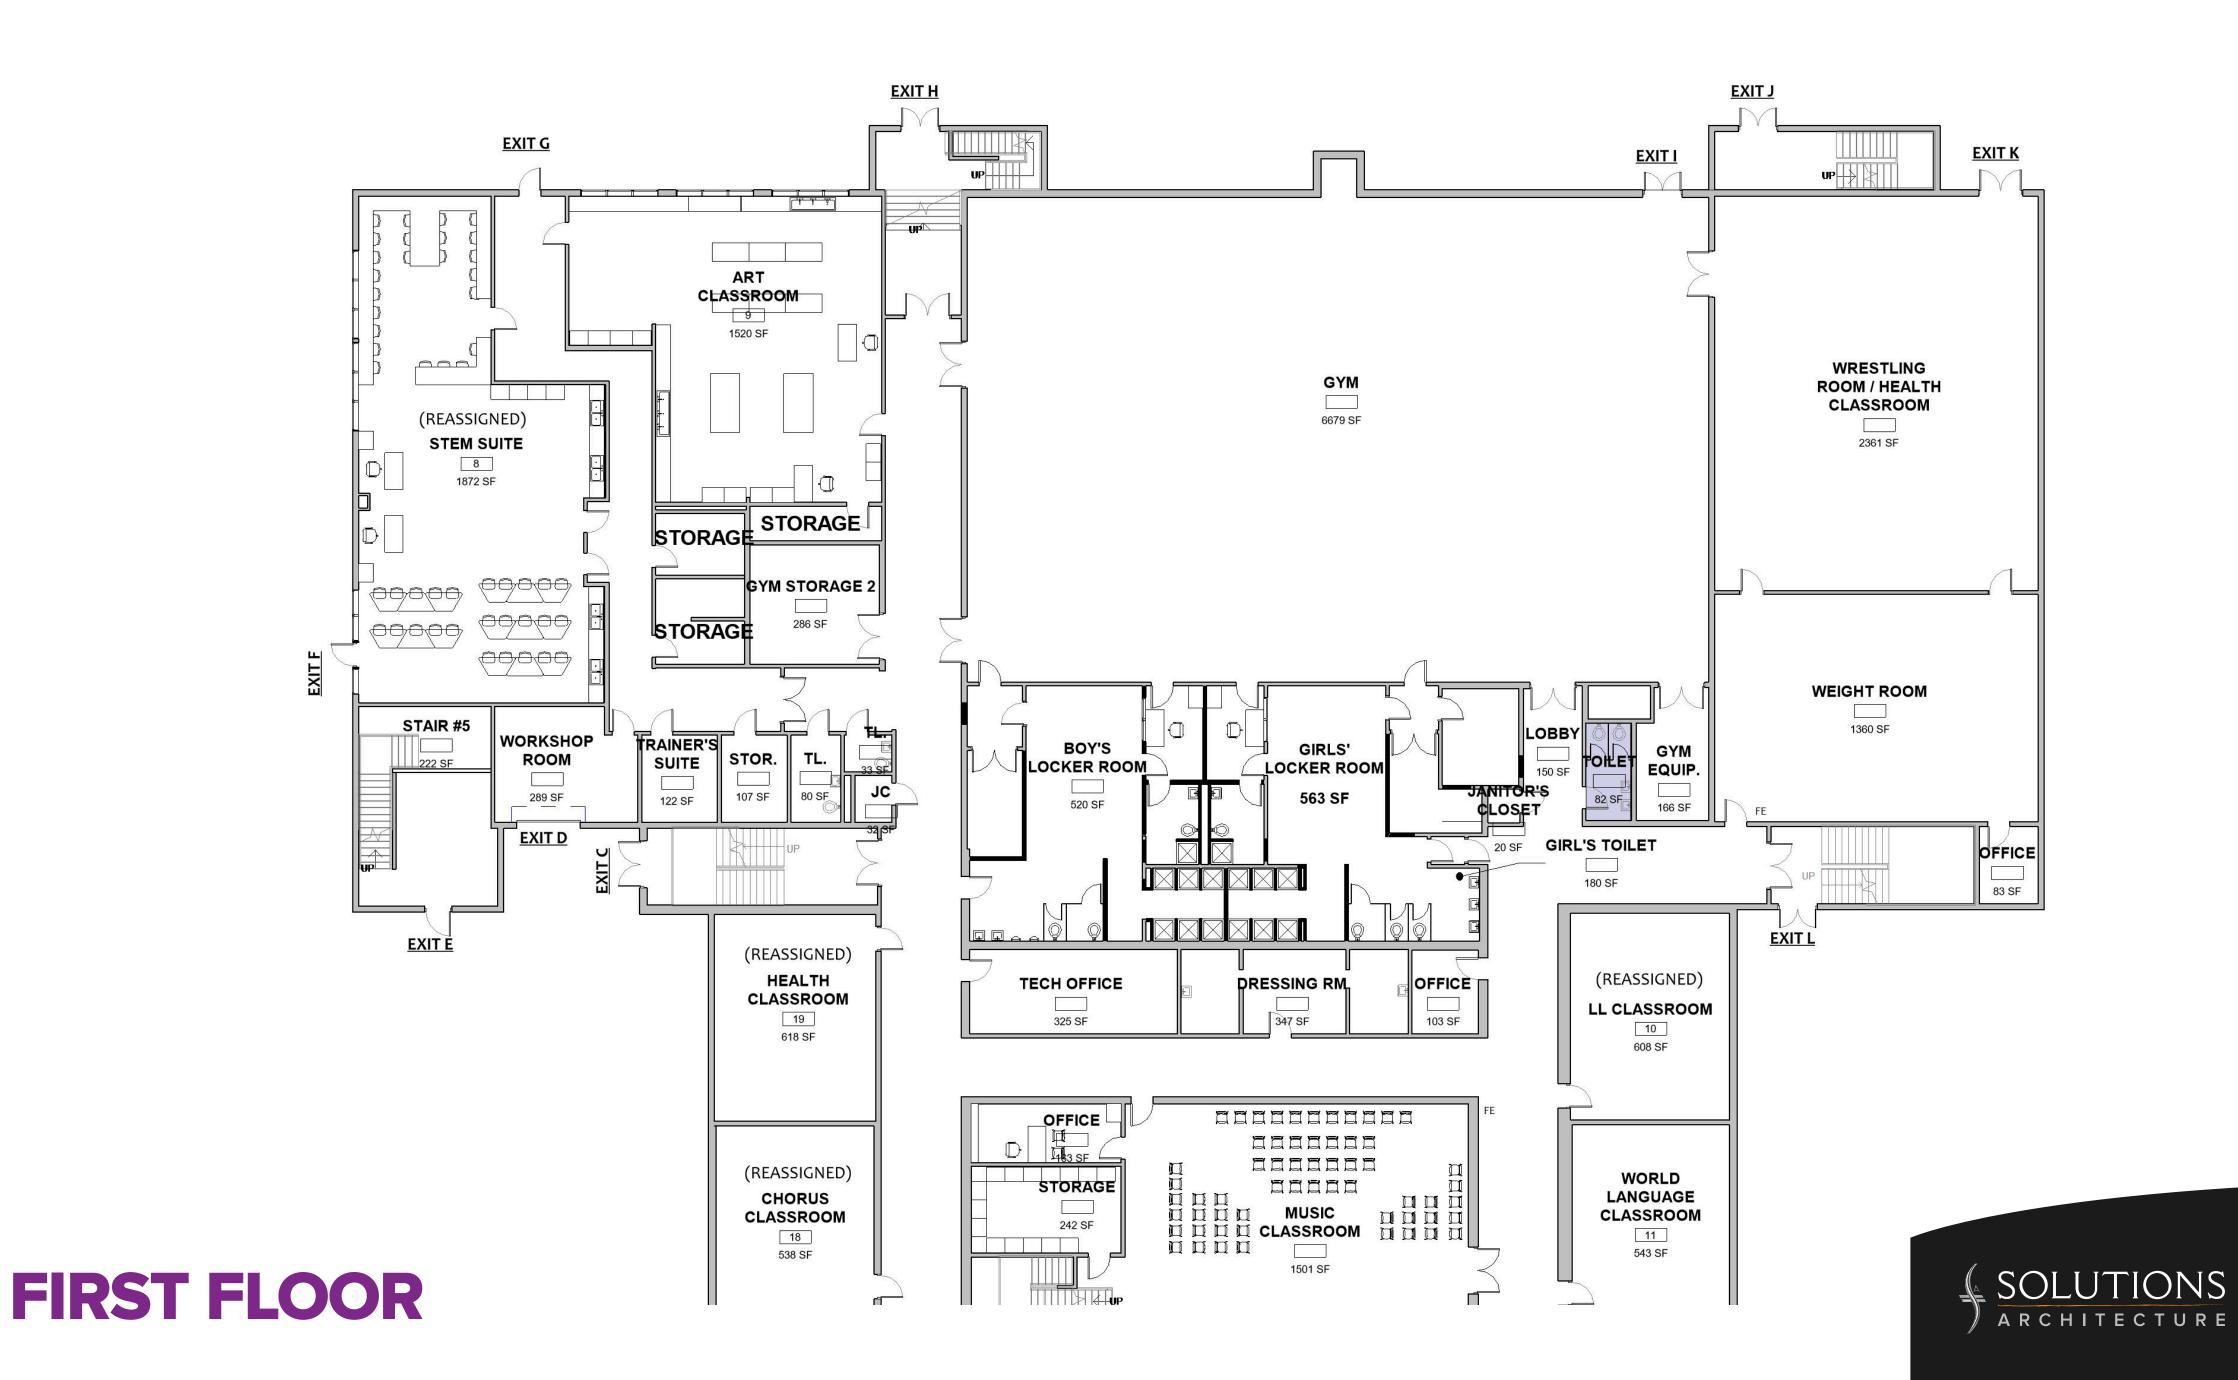

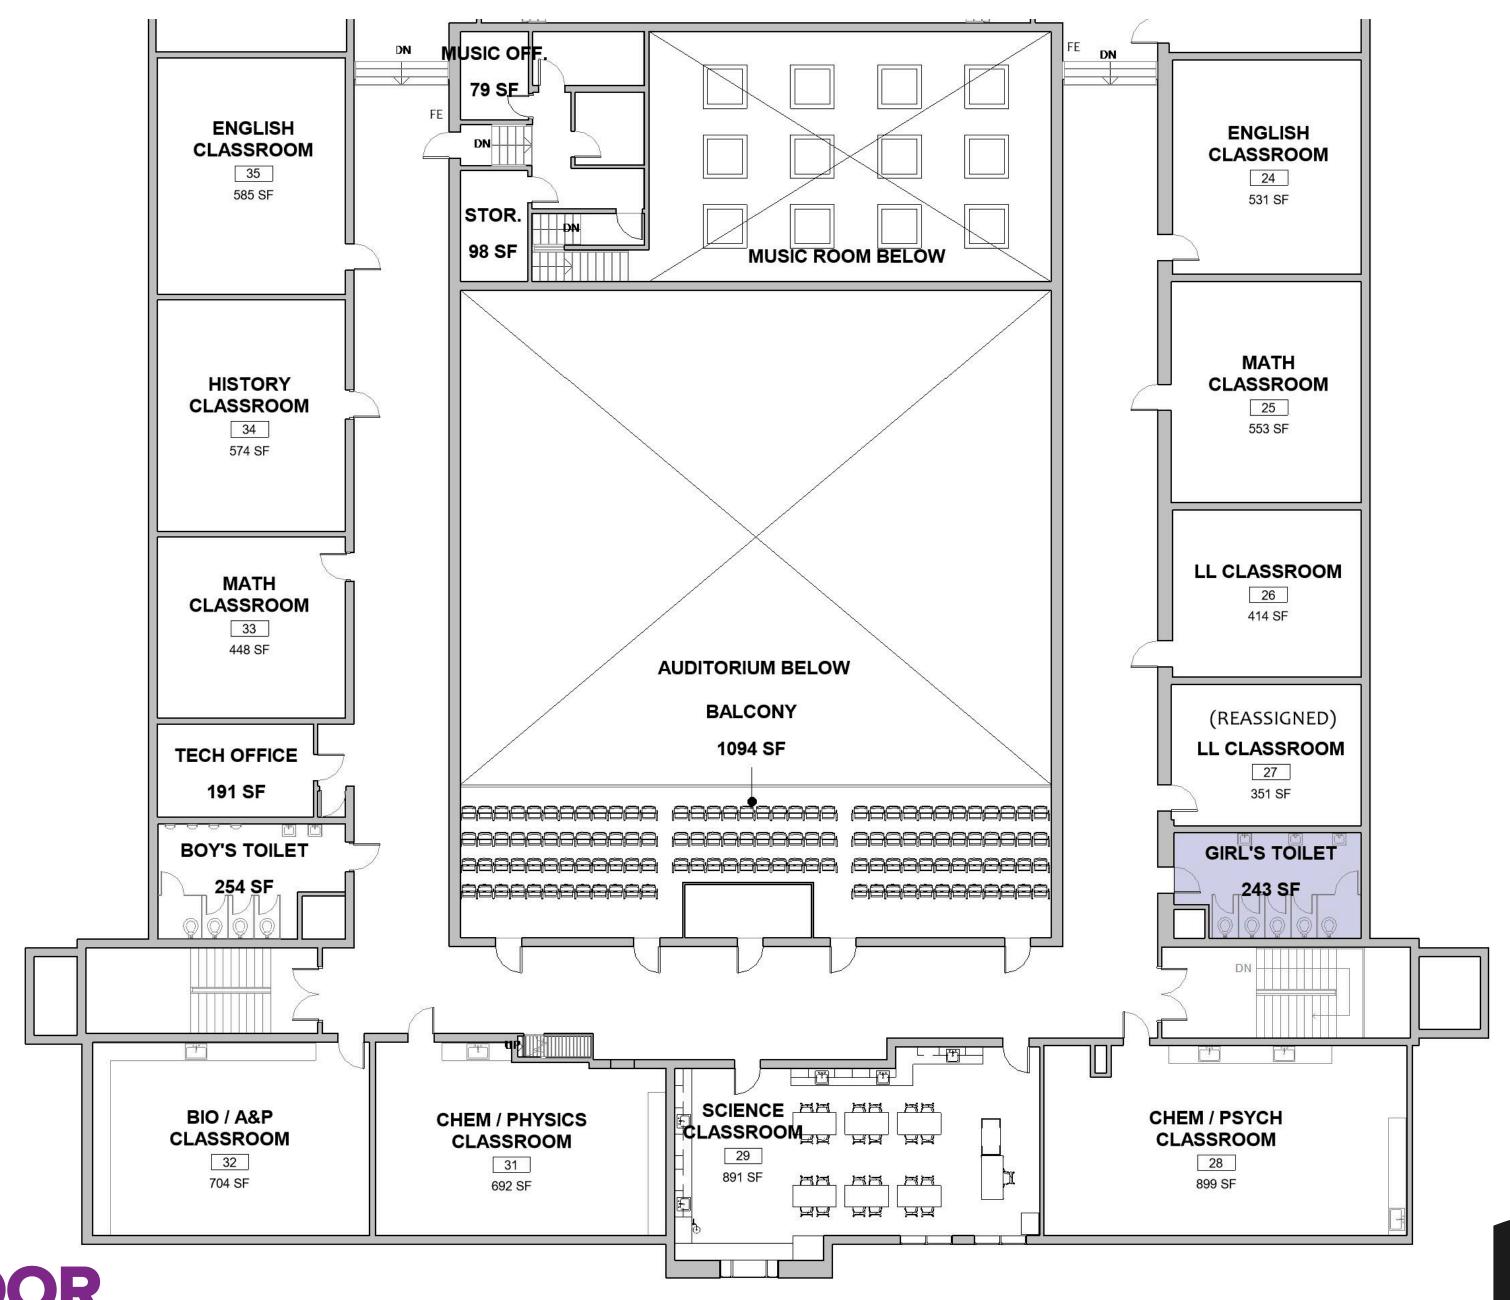



#### HS TOILETS TIMELINE



#### July

- » Review approach with School Admin
- » Determine the basis of design for MEP Systems

#### **A**ugust

- » Complete design and renderings
- » Finalize tile designs and fixture types

#### September

» Complete remaining Construction Documents

#### October

» Public Bidding Process

June'24 - September '24

» Complete renovation of 4 Toilets





For further information and to keep updated on the District-Wide Facilities Renovation Program Referendum, please scan the QR Code to the left or visit the district website: www.bogotaboe.com/referendum

## SOLUTIONS ARCHITECTURE www.solutions-arch.com 973-484-4800 (OFFICE)

